

Construction Updates at Perley Health

Edition:

5


September 10, 2025

Your Safety is Our Top Priority

Your safety is paramount throughout this project. Please help us keep everyone safe by paying close attention to all signs and following all safety directions in and around construction areas.

This is the fifth edition of our regular "construction" newsletter, designed to keep you informed about work details, safety measures, and project schedules.

Construction Overview

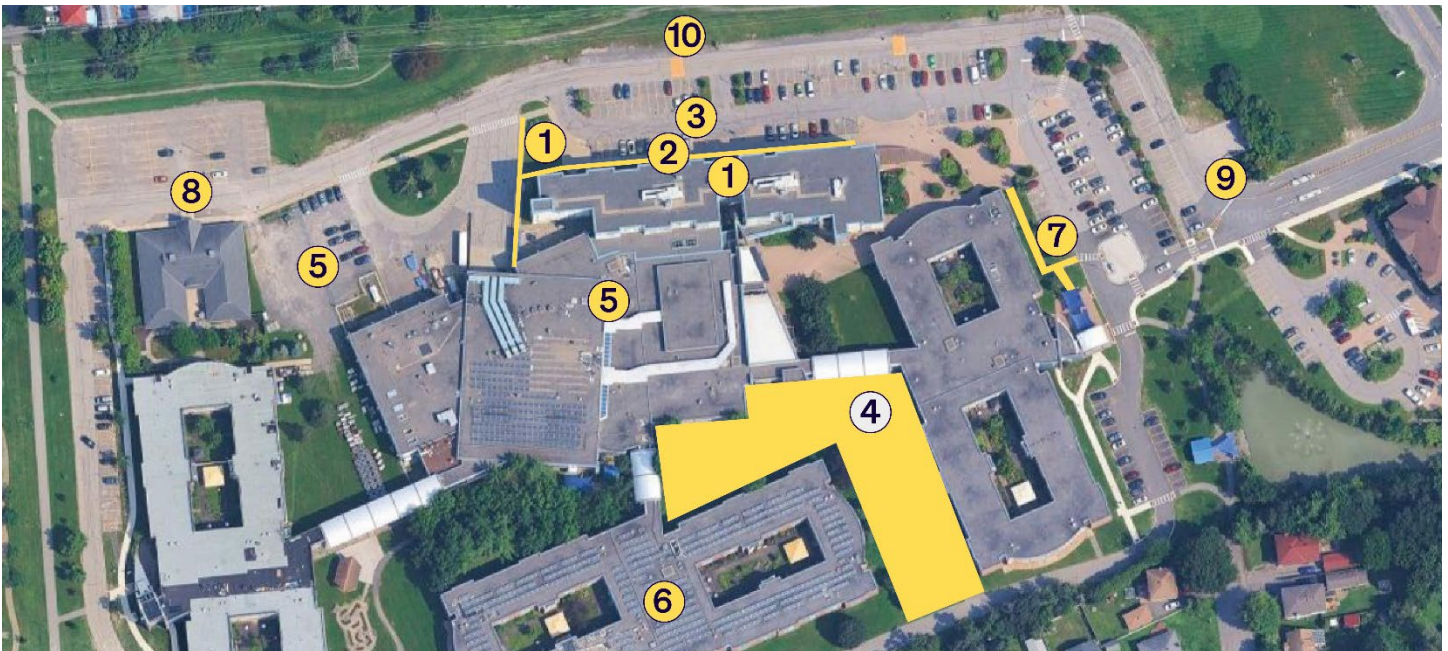

Current Work in Progress

1. New sidewalks at 1720 Russell Road, Commissionaires Ottawa Place to the staff entrance near the loading dock.
2. Patio stones installed near the main entrance at Commissionaires Ottawa Place.
3. Electric Vehicle Charging Stations: Electrical work begins for the installation of four parking spaces with electric vehicle charging stations.
4. Perley Health Intergenerational Child Care, a program of Andrew Fleck Children's Services. See reverse for details.
5. Re-roofing of Perley Centre. Parking lot next to Respite House unavailable to accommodate work.
6. **Ottawa Residence re-roofing is complete.**

Upcoming Projects

7. New sidewalks planned for Rideau Veterans Residence.
8. Temporary sidewalk repairs at Respite House.
9. Campus map re-installation.
10. Landscaping maintenance planned for Commissionaires Ottawa Place.
 - **1780 Russell Road landscaping complete.**

Important Service Disruptions

Intergenerational Child Care Update:

Piling Work

Piling work (drilling into the ground) has been completed.



Interior Demolition - Noise and Vibrations

Interior selective demolition will continue throughout the week and may cause intermittent noise in specific areas.

If needed, free hearing protection (ear plugs) is available at the Support Services offices on the second floor of the Perley Centre.

Staff Entrance Now Open

The staff entrance reopened **Friday, September 5**. Thank you for your patience during this work.

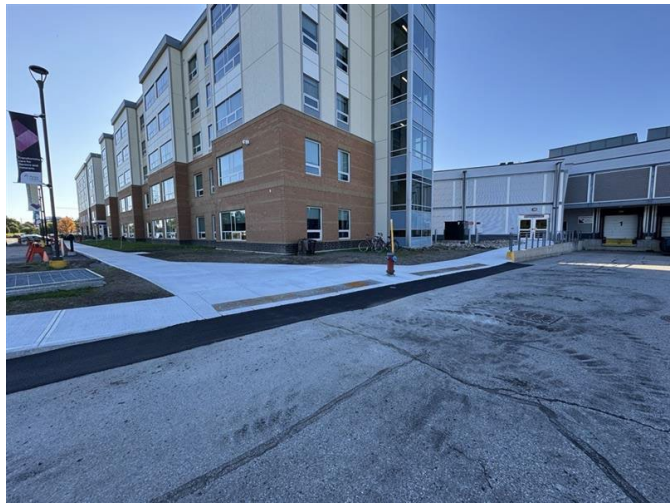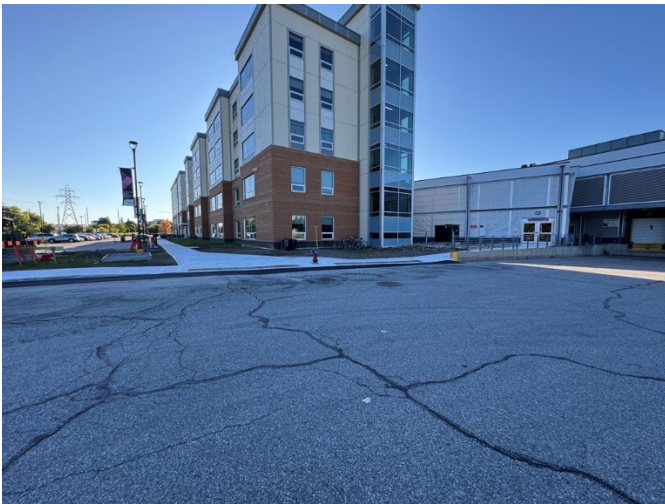

Roofing Updates

The Ottawa Residence Roof is now complete. Updates to Perley Health centre will begin **Wednesday, September 10th, 2025**. This work entails removal of the gravel on the roof and replacement. The work is expected to be ongoing throughout autumn.

Staff Parking Disruption

Commencing **Wednesday, September 10th**, the area adjacent to Respite House at Perley Health will be cordoned off to accommodate heavy equipment and the supplies required for installation of the new roof. Parking on the gravel lot will be unavailable during this time. Please park in other available staff parking locations.

For questions or concerns, please contact info@PerleyHealth.ca.

Perley Health produces a construction newsletter every two weeks, or when news must be promptly shared. This information is available in print throughout the Perley community and posted to the Perley Health website (PerleyHealth.ca/public-announcement).
