

Construction Updates at Perley Health

Edition:

8


October 21, 2025

Your Safety is Our Top Priority

Your safety is paramount throughout this project. Please help us keep everyone safe by paying close attention to all signs and following all safety directions in and around construction areas.

Free hearing protection is available from the Support Services offices on the second floor of the Perley Centre for anyone affected by the noise disruptions construction may cause.

Welcome to the eighth edition of our construction newsletter, designed to keep the Perley Health community informed on project schedules, work details, and safety measures across the campus.

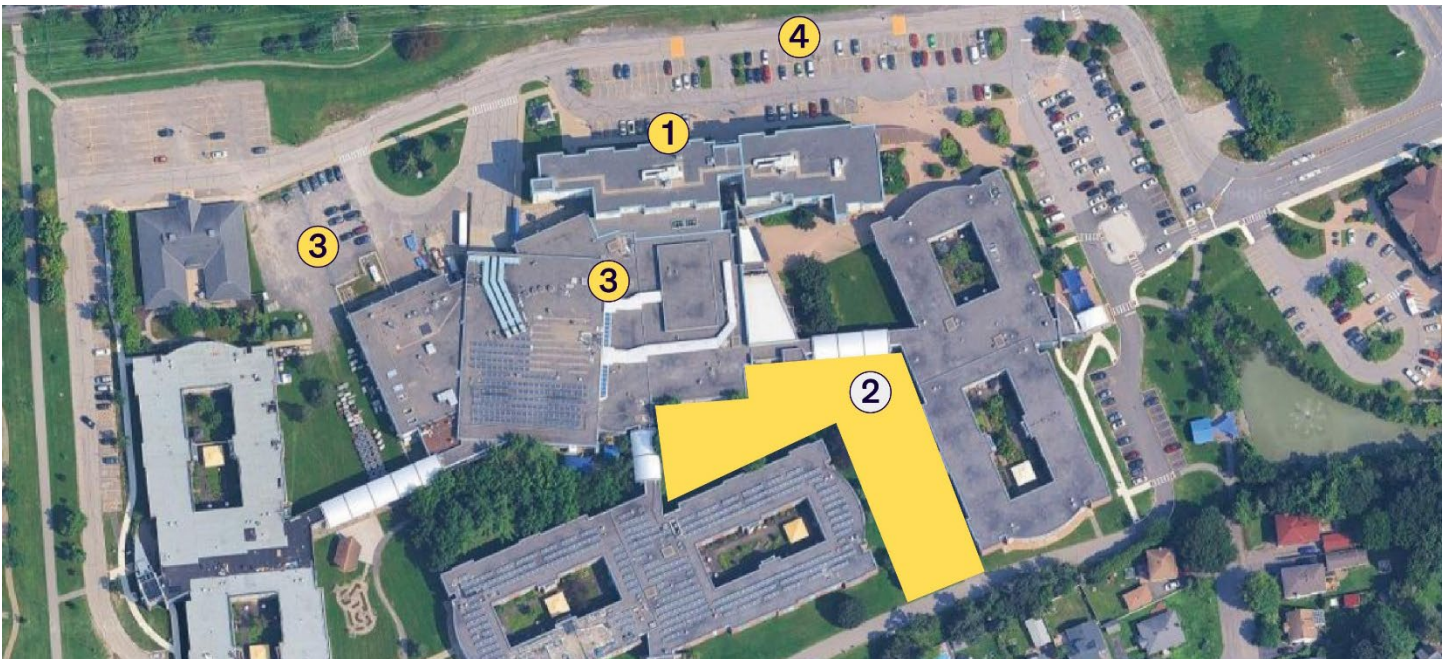

In Progress

1. **Charging Stations:** The Installation of four charging stations adjacent to four parking spaces continues near the entrance to Commissionaires Ottawa Place.
2. **Intergenerational Child Care:** Construction continues inside Perley Health and in the adjacent courtyard. For specifics, see the detailed update on page 2.
3. **Perley Centre Re-roofing:** This project is ongoing and is expected to continue through the Fall. The staff parking lot next to Respite House remains closed to accommodate the work. Please use other designated staff parking locations (find a map at PerleyHealth.ca/map).

Upcoming Work

4. **Upcoming Parking Lot Line Painting:** Line painting and numbering of assigned parking spots will take place in the parking lot on **October 29th and 30th**. Certain areas of the parking lot will be temporarily blocked off to allow this work to be completed safely and efficiently.

Intergenerational Child Care Update (Project Completion: 28%)

Construction continues on the Perley Health Intergenerational Child Care centre, a program of Andrew Fleck Children's Services.

Progress

- **Indoor:** Underground plumbing work is ongoing.
- **Outdoor:** (Courtyard between Ottawa Residence and Rideau Veterans Residence):
 - Relocation of the storm water line is complete.
 - Installation of the steel framing is complete.
 - Framing and roof installation for the new structure are progressing.



Outside Work - The courtyard bordered by the Rideau Veterans Residence and Ottawa Residence

Interior Impacts

Work has begun to connect the roof of the new child care centre to the main Perley building. This will require a temporary closure and some disruption on the second floor:

- **Art Studios Closure:** The two studios will be closed to allow us to temporarily remove windows and connect the new structure to Perley Centre.
 - The studios will close effective Saturday, October 25 and are expected to re-open on Monday, November 10.
 - Studio programs will be temporarily reassigned to other resident activity areas where possible.
 - Please check the Activity Boards and calendars on each unit, and the notices posted on the studio doors, for updated information.
- **Ottawa Residence Link, Second Floor:**
 - To safely connect the new building, a protective hoarding wall will be installed in the hallway of the Ottawa Residence second-floor link.
 - These walls are similar to the ones currently outside the pharmacy on the first floor.
 - These walls will limit some of the window viewing areas on the second floor.

Stay Informed

We produce a construction newsletter every two weeks, or whenever urgent news needs to be shared.

- **In Print:** Copies are available throughout the Perley Health community.
- **Online:** Visit our website's Urgent News information page: PerleyHealth.ca/public-announcement.

For questions or concerns, please contact info@PerleyHealth.ca.
